

Conduit Test plan

Introduction

1. Test strategy

- 1.1 Testing scope
 - 1.1.1 Features to be tested
 - 1.1.2 Out of test scope
- 1.2 Test types
- 1.3 Risks and Issues
- 1.4 Test Logistics
 - 1.4.1 Who will test?
 - 1.4.2 When will the testing occur?

2. Test objective

3. Test criteria

- 3.1 Suspension Criteria
- 3.2 Exit criteria

4. Resource Planning

- 4.1 System Resource
- 4.2 Human resource

5. Test Environment

6. Schedule & estimation

- 6.1 All project tasks and estimation
- 6.2 Schedule to complete these tasks

7. Test deliverables

- 7.1 Before the testing phase
- 7.2 During the testing
- 7.3 After the testing cycle is over

Introduction

The “Conduit” application is designed as an open-source application to train software development and testing skills. The main website functionality includes registration and sign-in, posting articles on different topics, reading articles, the ability to like an article, posting a comment, and following users.

The Test Plan is designed to prescribe the scope, approach, resources, and schedule of all testing activities of the “Conduit” website.

The plan identifies the features to be tested, the types of testing to be performed, the resources and schedule required to complete testing, and the risks associated with the plan.

1. Test strategy

1.1 Testing scope

1.1.1 Features to be tested

Module name	Login type	Description
Conduit logo	Logged in	Validate that the Conduit logo is displayed correctly and redirects users to the Home page when clicked. Verify that the user remains authenticated after the redirection.
Conduit logo	Logged out	Validate that the Conduit logo is displayed correctly and redirects users to the Home page when clicked.
Home	Logged in	Validate that feeds, content and user-specific features are available to authenticated users. Verify that authenticated users can add comments, follow users and favorite articles.
Home	Logged out	Validate that public content is correctly displayed to non-authenticated users. Verify that non-authenticated users are

		redirected to the sign in page after trying to interact with the platform.
Sign in		Validate that the Sign In page is displayed correctly and allows existing users to log in with valid credentials. Verify that access is denied when invalid credentials are provided and that users can navigate to the Sign Up page.

1.1.2 Out of test scope

These areas are out of scope for this testing cycle:

- Website Security
- Website Performance
- Website API testing
- Test Automation

1.2 Test types

In this testing cycle, the Conduit website will be tested using the next testing types:

- System testing: all the testing will be conducted on a complete, integrated system to evaluate the system's compliance with its specified requirements.
 - Exploratory testing.
 - Smoke testing for each new build.
 - Functional testing of all the features
 - GUI testing
 - Compatibility testing: test only Windows and MacOS browsers

1.3 Risks and Issues

Risk	Mitigation
Team members lack the required skills for website testing	Provide training, mentoring and support to ensure that the team members have the required skills to execute tests.
Not enough time to test all browsers and OS.	Prioritize tests on the most commonly used browsers and operating systems.
Not enough time to execute all test scenarios.	Prioritize critical and high-risk test scenarios.
A member of the team has got sick	Train at least 2-3 team members in all parts of the testing process to ensure coverage during absences.

1.4 Test Logistics

1.4.1 Who will test?

1.4.2 When will the testing occur?

The team will start the testing after:

2. Test objective

The test objectives are to verify the functionality and API of the Conduit app. The testing should be focused on the flow of publishing articles and sharing information between members. The main features are authorization, posting new articles, following members, saving favorite articles on their pages, adding likes, and writing comments. Testing should be done on preselected versions of browsers and mobile devices described in the "System resource" section.

3. Test criteria

3.1 Suspension criteria

- 10% of P0/P1 tests failed, which should lead to the testing suspension until the development team fixes all the corresponding bugs.
- 30% of P2/P3 tests failed, which should lead to the testing suspension until the development team fixes all the corresponding bugs.

3.2 Exit criteria

The test execution will be stopped no later than the last day of the sprint. The exit criteria should be met to complete the testing cycle:

- The mandatory Execution rate is 95%.
- The mandatory Pass rate is 100% for P0/P1 tests.
- The mandatory Pass rate is 80% for P2/P3 tests.
- All necessary artifacts collected: test cases, and bug reports.
- The product should not have known bugs with severity Critical and Major and bugs with Priority High at the time of finishing testing.
- The list of allowed bugs is agreed upon with the developers and managers.

4. Resource planning

4.1 System resources

No.	Resources	Description
1	Browser	Most commonly used browsers required to access and teste the application.
2	Network	Stable internet required to access and test the application.


3	Computer	Notebook or desktop required to access and test the application.
---	----------	--

4.2 Human resources

No.	Resources	Description of tasks
1	QA members	Plan, analyze, create, and execute tests, report bugs, and verify bug fixes.
2	Mentors	Provide guidance, support, feedback and review testing deliverables during the testing process.

5. Test environment

Testing should be conducted in the production environment. To run the app locally for working with DB we will use Docker.

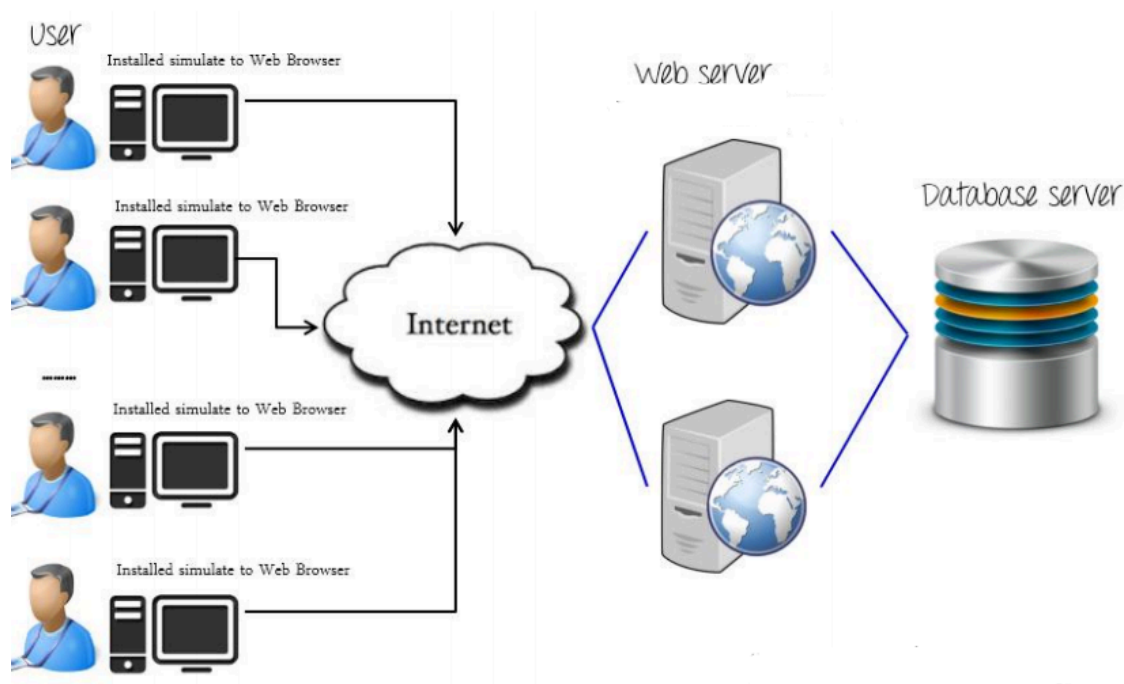

6. Schedule & estimation

6.1 All project tasks and estimation

Task	Members	Estimate effort
Create Test plan	QA members	3 man-hour
Create decomposition, decision table, state transition diagram	QA members	2-3 man-hour
Create Test cases	QA members	4-5 man-hour
Review Test cases	Mentors	1 man-hour
Test cases execution	QA members	2-3 man-hour
Create Bug reports	QA members	1-2 man-hour
Writing test report	QA members	1 man-hour

6.2 Schedule to complete these tasks

Task	1-st Sprint	2-nd Sprint	3-rd Sprint
Create Test plan	☒		
Create decomposition, decision table, state transition diagram	☒		
Create Test cases		☒	
Review Test cases		☒	
Test cases execution			☒
Create Bug reports			☒
Writing and preparing test results			☒

7. Test deliverables

7.1 Before the testing phase

- Test Plan
- Test Cases
- Decomposition
- Decision Table
- State Transition Diagram

7.2 During the testing

- Bug Reports
- Text Execution Results

7.3 After the testing cycle is over

- Test Report
- Test Summary Report
